
Activity ID	Activity Name	Original Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Predecess	Successors
LADERA	**Ladera Golf Club**	548	548	0%	15-Jan-27	20-Feb-29	0		
LADERA.1	**General Requirements**	25	25	0%	15-Jan-27	18-Feb-27	0		
A1000	Supervision & Project Management	5	5	0%	15-Jan-27	21-Jan-27	0		A1010
A1010	Permits & Approvals	5	5	0%	22-Jan-27*	28-Jan-27	0	A1000	A1020
A1020	Mobilization	3	3	0%	29-Jan-27*	02-Feb-27	0	A1010	A1030
A1030	Bonds & Insurance	2	2	0%	03-Feb-27*	04-Feb-27	0	A1020	A1040
A1040	Temporary Facilities	5	5	0%	05-Feb-27*	11-Feb-27	0	A1030	A2000
A2000	Scaffolding	5	5	0%	12-Feb-27*	18-Feb-27	0	A1040	A1050
LADERA.2	**Existing Condition**	31	31	0%	19-Feb-27	02-Apr-27	0		
A1050	Demolish & Remove Asphalt	5	5	0%	19-Feb-27*	25-Feb-27	0	A2000	A1060
A1060	Remove Lot Light	2	2	0%	26-Feb-27*	01-Mar-27	0	A1050	A2080
A1070	Demolish & Remove Steel Canopy	3	3	0%	04-Mar-27*	08-Mar-27	0	A2080	A1080
A1080	Decommission & Remove Modular Build	5	5	0%	09-Mar-27*	15-Mar-27	0	A1070	A1090
A1090	Demolish & Remove Fence	3	3	0%	16-Mar-27*	18-Mar-27	0	A1080	A2010
A2010	Remove Fire Hydrant	2	2	0%	19-Mar-27*	22-Mar-27	0	A1090	A2020
A2020	Demolish & Remove Bollards	2	2	0%	23-Mar-27*	24-Mar-27	0	A2010	A2030
A2030	Remove Trailer / Canopy	2	2	0%	25-Mar-27*	26-Mar-27	0	A2020	A2040
A2040	Remove Fence Double Gate	2	2	0%	29-Mar-27*	30-Mar-27	0	A2030	A2050
A2050	Hauling for Demolition Work	3	3	0%	31-Mar-27*	02-Apr-27	0	A2040	A1100
A2080	Blind Flange	2	2	0%	02-Mar-27*	03-Mar-27	0	A1060	A1070
LADERA.3	**Earthwork**	30	30	0%	05-Apr-27	14-May-27	0		
A1100	Excavation	10	10	0%	05-Apr-27*	16-Apr-27	0	A2050	A1110
A1110	Rough Grading	5	5	0%	19-Apr-27*	23-Apr-27	0	A1100	A1120
A1120	Fill Placement	5	5	0%	26-Apr-27*	30-Apr-27	0	A1110	A1130
A1130	Compaction	5	5	0%	03-May-27*	07-May-27	0	A1120	A1140
A1140	Backfilling	5	5	0%	10-May-27*	14-May-27	0	A1130	A1150
LADERA.4	**Utilities**	27	27	0%	17-May-27	22-Jun-27	0		
A1150	Storm Drain Installation	8	8	0%	17-May-27*	26-May-27	0	A1140	A1160
A1160	Sanitary Sewer Installation	6	6	0%	27-May-27*	03-Jun-27	0	A1150	A1170
A1170	Water Line Installation	5	5	0%	04-Jun-27*	10-Jun-27	0	A1160	A1180
A1180	Utility Connections	5	5	0%	11-Jun-27*	17-Jun-27	0	A1170	A1190
A1190	Utility Testing	3	3	0%	18-Jun-27*	22-Jun-27	0	A1180	A1200
LADERA.5	**Concrete**	48	48	0%	23-Jun-27	27-Aug-27	0		
A1200	Pad Footings	5	5	0%	23-Jun-27*	29-Jun-27	0	A1190	A1210
A1210	Concrete Column Bases	4	4	0%	30-Jun-27*	05-Jul-27	0	A1200	A1220
A1220	Perimeter Footings	5	5	0%	06-Jul-27*	12-Jul-27	0	A1210	A1230
A1230	Stem Walls	6	6	0%	13-Jul-27*	20-Jul-27	0	A1220	A1240
A1240	Grade Beams	5	5	0%	21-Jul-27*	27-Jul-27	0	A1230	A1250
A1250	Moist Sand Layer	2	2	0%	28-Jul-27*	29-Jul-27	0	A1240	A1260
A1260	Slab on Grade	10	10	0%	30-Jul-27*	12-Aug-27	0	A1250	A1270
A1270	Concrete Side Walks	5	5	0%	13-Aug-27*	19-Aug-27	0	A1260	A2090
A2090	Equipment Pads	3	3	0%	20-Aug-27*	24-Aug-27	0	A1270	A2100
A2100	Concrete Repair & Patching	3	3	0%	25-Aug-27*	27-Aug-27	0	A2090	A1280
LADERA.6	**Metals**	31	31	0%	30-Aug-27	11-Oct-27	0		
A1280	Structural Steel Fabrication	10	10	0%	30-Aug-27*	10-Sep-27	0	A2100	A1290
A1290	Structural Steel Erection	10	10	0%	13-Sep-27*	24-Sep-27	0	A1280	A1300
A1300	Metal Deck Installation	5	5	0%	27-Sep-27*	01-Oct-27	0	A1290	A1310
A1310	Stairs Installation	3	3	0%	04-Oct-27*	06-Oct-27	0	A1300	A1320
A1320	Railings Installation	3	3	0%	07-Oct-27*	11-Oct-27	0	A1310	A1330
LADERA.7	**Wood Plastics & Composite**	38	38	0%	12-Oct-27	02-Dec-27	0		
A1330	Wood Framing	12	12	0%	12-Oct-27*	27-Oct-27	0	A1320	A1340
A1340	Sheathing Installation	5	5	0%	28-Oct-27*	03-Nov-27	0	A1330	A1350
A1350	Wood Blocking	3	3	0%	04-Nov-27*	08-Nov-27	0	A1340	A1360
A1360	Door Frame Install	3	3	0%	09-Nov-27*	11-Nov-27	0	A1350	A1370
A1370	Finish Carpentry	5	5	0%	12-Nov-27*	18-Nov-27	0	A1360	A1380
A1380	Millwork Installation	5	5	0%	19-Nov-27*	25-Nov-27	0	A1370	A1390
A1390	Casework Installation	5	5	0%	26-Nov-27*	02-Dec-27	0	A1380	A1400

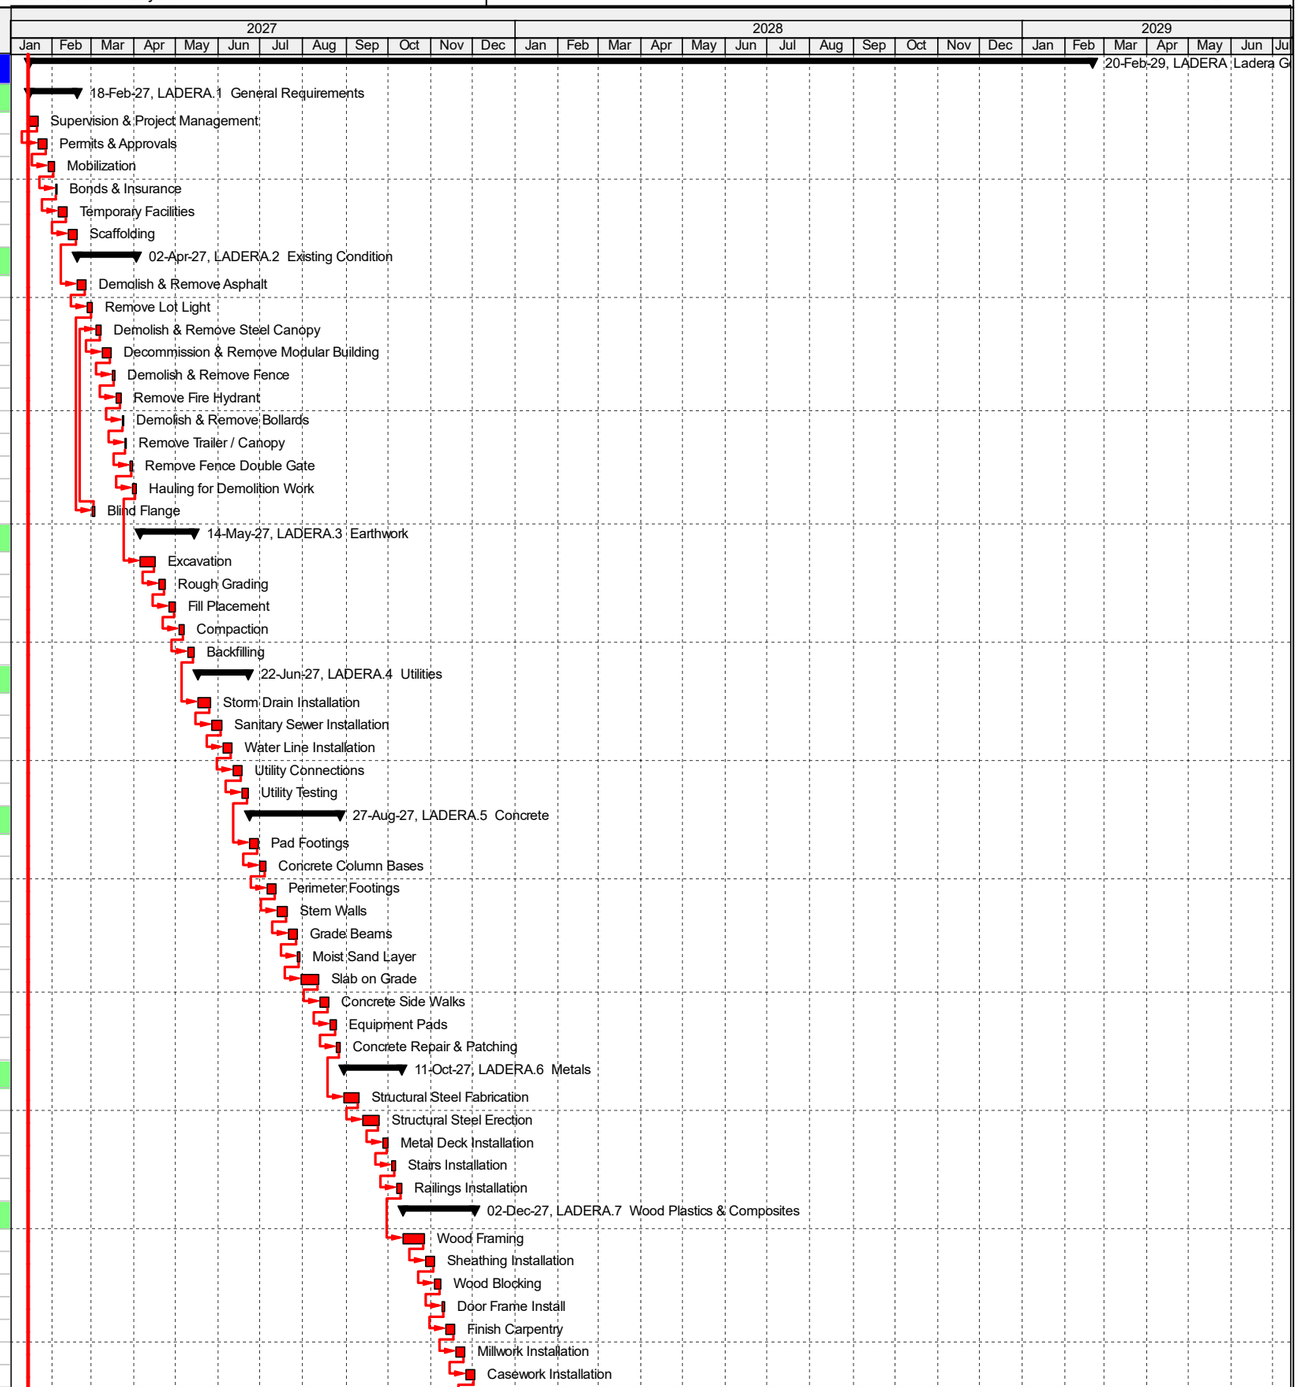


Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Predecess	Successors
LADERA.8	**Thermal & Moisture Protecti**	26	26	0%	03-Dec-27	07-Jan-28	0		
A1400	Waterproofing	5	5	0%	03-Dec-27*	09-Dec-27	0	A1390	A1410
A1410	Roofing	10	10	0%	10-Dec-27*	23-Dec-27	0	A1400	A1420
A1420	Insulation	5	5	0%	24-Dec-27*	30-Dec-27	0	A1410	A1430
A1430	Flashing Installation	3	3	0%	31-Dec-27*	04-Jan-28	0	A1420	A1440
A1440	Sealants	3	3	0%	05-Jan-28*	07-Jan-28	0	A1430	A1450
LADERA.9	**Openings**	34	34	0%	10-Jan-28	24-Feb-28	0		
A1450	Hollow Metal Frames	3	3	0%	10-Jan-28*	12-Jan-28	0	A1440	A1460
A1460	Exterior Doors	5	5	0%	13-Jan-28*	19-Jan-28	0	A1450	A1470
A1470	Imterior Doors	5	5	0%	20-Jan-28*	26-Jan-28	0	A1460	A1480
A1480	Aluminum Storefront	5	5	0%	27-Jan-28*	02-Feb-28	0	A1470	A1490
A1490	Windows Installation	5	5	0%	03-Feb-28*	09-Feb-28	0	A1480	A1500
A1500	Overhead Doors	3	3	0%	10-Feb-28*	14-Feb-28	0	A1490	A1510
A1510	Door Hardware	3	3	0%	15-Feb-28*	17-Feb-28	0	A1500	A1520
A1520	Glazing	5	5	0%	18-Feb-28*	24-Feb-28	0	A1510	A1530
LADERA.10	**Finishes**	65	65	0%	25-Feb-28	25-May-28	0		
A1530	Drywall Installation	15	15	0%	25-Feb-28*	16-Mar-28	0	A1520	A1540
A1540	Acoustical Ceilings	10	10	0%	17-Mar-28*	30-Mar-28	0	A1530	A1550
A1550	Ceramic Tile	10	10	0%	31-Mar-28*	13-Apr-28	0	A1540	A1560
A1560	Resilient Flooring	10	10	0%	14-Apr-28*	27-Apr-28	0	A1550	A1570
A1570	Painting	10	10	0%	28-Apr-28*	11-May-28	0	A1560	A1580
A1580	Wall Finishes	5	5	0%	12-May-28*	18-May-28	0	A1570	A1590
A1590	Finish Carpentry	5	5	0%	19-May-28*	25-May-28	0	A1580	A1600
LADERA.11	**Specialities**	11	11	0%	26-May-28	09-Jun-28	0		
A1600	Toilet Accessories	3	3	0%	26-May-28*	30-May-28	0	A1590	A1610
A1610	Signage	2	2	0%	31-May-28*	01-Jun-28	0	A1600	A1620
A1620	Fire Extinguishers	2	2	0%	02-Jun-28*	05-Jun-28	0	A1610	A1630
A1630	Corner Guards	2	2	0%	06-Jun-28*	07-Jun-28	0	A1620	A1640
A1640	Final Accessories	2	2	0%	08-Jun-28*	09-Jun-28	0	A1630	A1650
LADERA.12	**Equipments**	15	15	0%	12-Jun-28	30-Jun-28	0		
A1650	Equipment Delivery	3	3	0%	12-Jun-28*	14-Jun-28	0	A1640	A1660
A1660	Equipment Installation	5	5	0%	15-Jun-28*	21-Jun-28	0	A1650	A1670
A1670	Equipment Connections	3	3	0%	22-Jun-28*	26-Jun-28	0	A1660	A1680
A1680	Equipment Testing	2	2	0%	27-Jun-28*	28-Jun-28	0	A1670	A1690
A1690	Equipment Commissioning	2	2	0%	29-Jun-28*	30-Jun-28	0	A1680	A1700
LADERA.13	**Plumbing**	34	34	0%	03-Jul-28	17-Aug-28	0		
A1700	Underground Plumbing	8	8	0%	03-Jul-28*	12-Jul-28	0	A1690	A1710
A1710	Rough-In Plumbing	15	15	0%	13-Jul-28*	02-Aug-28	0	A1700	A1720
A1720	Plumbing Fixtures	5	5	0%	03-Aug-28*	09-Aug-28	0	A1710	A1730
A1730	Final Connections	3	3	0%	10-Aug-28*	14-Aug-28	0	A1720	A1740
A1740	Testing & Commissioning	3	3	0%	15-Aug-28*	17-Aug-28	0	A1730	A1750
LADERA.14	**HVAC**	36	36	0%	18-Aug-28	06-Oct-28	0		
A1750	Ductwork Installation	15	15	0%	18-Aug-28*	07-Sep-28	0	A1740	A1760
A1760	HVAC Equipment Installation	8	8	0%	08-Sep-28*	19-Sep-28	0	A1750	A1770
A1770	Controls Installation	5	5	0%	20-Sep-28*	26-Sep-28	0	A1760	A1780
A1780	Testing & Balancing	5	5	0%	27-Sep-28*	03-Oct-28	0	A1770	A1790
A1790	HVAC Commissioning	3	3	0%	04-Oct-28*	06-Oct-28	0	A1780	A1800
LADERA.15	**Electrical**	48	48	0%	09-Oct-28	13-Dec-28	0		
A1800	Underground Electrical	5	5	0%	09-Oct-28*	13-Oct-28	0	A1790	A1810
A1810	Site Lighting	5	5	0%	16-Oct-28*	20-Oct-28	0	A1800	A1820
A1820	Conduits & Cabling	15	15	0%	23-Oct-28*	10-Nov-28	0	A1810	A1830
A1830	Panel Installation	5	5	0%	13-Nov-28*	17-Nov-28	0	A1820	A1840
A1840	Lighting Installation	5	5	0%	20-Nov-28*	24-Nov-28	0	A1830	A1850
A1850	Devices Installation	5	5	0%	27-Nov-28*	01-Dec-28	0	A1840	A2060
A2060	Controls & Low Voltage	5	5	0%	04-Dec-28*	08-Dec-28	0	A1850	A2070
A2070	Electrical Testing	3	3	0%	11-Dec-28*	13-Dec-28	0	A2060	A1860
LADERA.16	**Exterior Improvements**	23	23	0%	14-Dec-28	15-Jan-29	0		

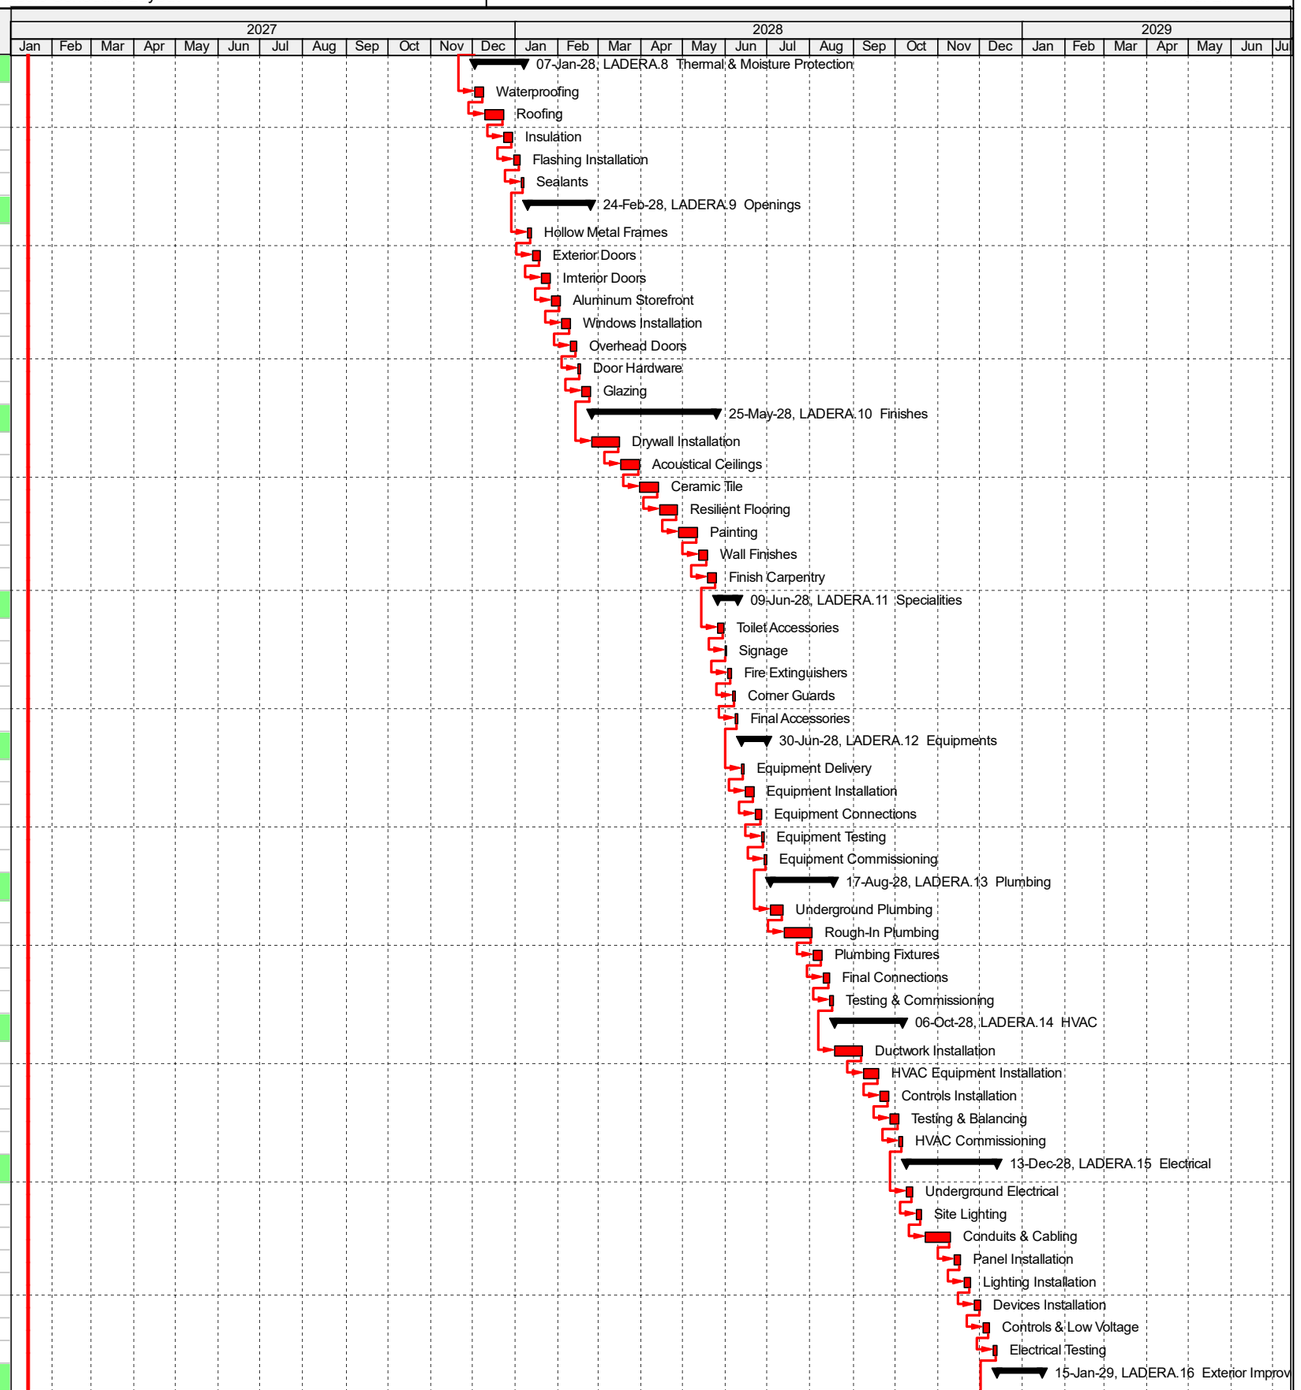


Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Predecess	Successors
A1860	Concrete Pavement	5	5	0%	14-Dec-28*	20-Dec-28	0	A2070	A1870
A1870	Asphalt Paving	5	5	0%	21-Dec-28*	27-Dec-28	0	A1860	A1880
A1880	Site Furnishings	3	3	0%	28-Dec-28*	01-Jan-29	0	A1870	A1890
A1890	Landscaping	5	5	0%	02-Jan-29*	08-Jan-29	0	A1880	A1900
A1900	Irrigation System	3	3	0%	09-Jan-29*	11-Jan-29	0	A1890	A1910
A1910	Final Site Cleanup	2	2	0%	12-Jan-29*	15-Jan-29	0	A1900	A1920
LADERA.17	**Closeout & Comissioning**	26	26	0%	16-Jan-29	20-Feb-29	0		
A1920	Integrated Systems Testing	5	5	0%	16-Jan-29*	22-Jan-29	0	A1910	A1930
A1930	MEP Commissioning	5	5	0%	23-Jan-29*	29-Jan-29	0	A1920	A1940
A1940	Final Inspections	3	3	0%	30-Jan-29*	01-Feb-29	0	A1930	A1950
A1950	Punch List Completion	5	5	0%	02-Feb-29*	08-Feb-29	0	A1940	A1960
A1960	Final Cleaning	3	3	0%	09-Feb-29*	13-Feb-29	0	A1950	A1970
A1970	Owner Training & O&M Manuals	3	3	0%	14-Feb-29*	16-Feb-29	0	A1960	A1980
A1980	Substantial Completion	1	1	0%	19-Feb-29*	19-Feb-29	0	A1970	A1990
A1990	Final Handover & Project Closeout	1	1	0%	20-Feb-29*	20-Feb-29	0	A1980	

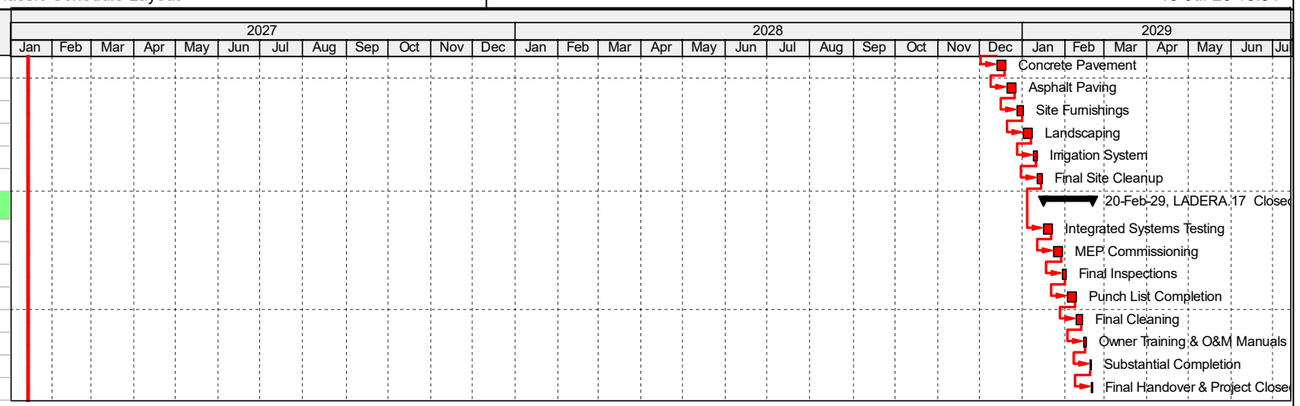

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation
